ID		ID	Task Name	Start
1		**0**	**Quarterly Reviews**	**Mon 31/03/03**
10		**1**	**ESO VISTA software deliverables and documentation**	**Wed 01/01/03**
12		0	Calibration plan document	Tue 01/07/03
13		0	Data Reduction Specification	Tue 01/07/03
14		0	DFS user requirements document	Tue 01/07/03
15		**2**	**Management and Defenition of Responsibilities**	**Wed 01/01/03**
24		0	ICD between CASU and JAC	Wed 31/12/03
25		0	ICD between CASU and WFAU	Tue 01/07/03
26		0	Fits headers and data structures defention document	Tue 01/07/03
27		**3**	**Pipeline Infrastructure and Progress Monitoring Tools**	**Wed 01/01/03**
35		0	Deliver pipeline V1.0	Wed 31/12/03
36		0	Deliver documentation for pipeline V1.0	Wed 31/12/03
37		**4**	**Set up and Manage Raw Science Archive**	**Wed 01/10/03**
40		0	Create Raw Science Archive	Wed 31/12/03
41		**5**	**Set up and Manage Data Processing System Hardware**	**Wed 01/01/03**
47		0	Processing hardware in place	Wed 31/12/03
48		**6**	**Run Standard Pipeline**	**Thu 01/01/04**
57		0	Data flow to WFAU initiated	Thu 01/01/04
58		**7**	**Development Work for Summit Pipeline**	**Wed 01/01/03**
63		0	Deliver summit pipeline	Wed 31/12/03
64		0	Deliver summit pipeline documentation	Wed 31/12/03
65		**8**	**Development and Testing of Standard 2D Processing**	**Wed 01/01/03**
73		0	Complete 2D processing modules V1.0	Tue 30/09/03
74		**9**	**Development and Testing of Standard Catalogue Products**	**Wed 01/01/03**
82		0	Complete standard catalogue modules V1.0	Tue 30/09/03
83		**10**	**Set Up, Trial and Run Further Processing Software**	**Wed 01/01/03**
91		0	Deliver 2D PSF and Sersic fitting applications	Fri 31/12/04
92		**11**	**Photometric Standards and Calibraion**	**Wed 01/01/03**
100		0	Allocate primary and secondary standard stars/fields	Sat 01/11/03
101		0	Photometric calibration and colour equations	Thu 01/07/04
102		**12**	**Further Development of DQC Measures**	**Wed 01/01/03**
107		**13**	**Co-located List Driven Photometry**	**Wed 01/01/03**
111		0	Deliver list driven photometer	Wed 31/12/03
112		**14**	**Stacking and Mosaicing**	**Wed 01/01/03**
118		0	Deliver basic stacker and mosaicer	Tue 30/09/03
119		**15**	**Continuum Subtraction and Basic Difference Imaging**	**Wed 01/01/03**
124		**16**	**Interpolation Techniques and PSF Modelling**	**Wed 01/01/03**
130		0	Deliver PSF photometer	Fri 31/12/04

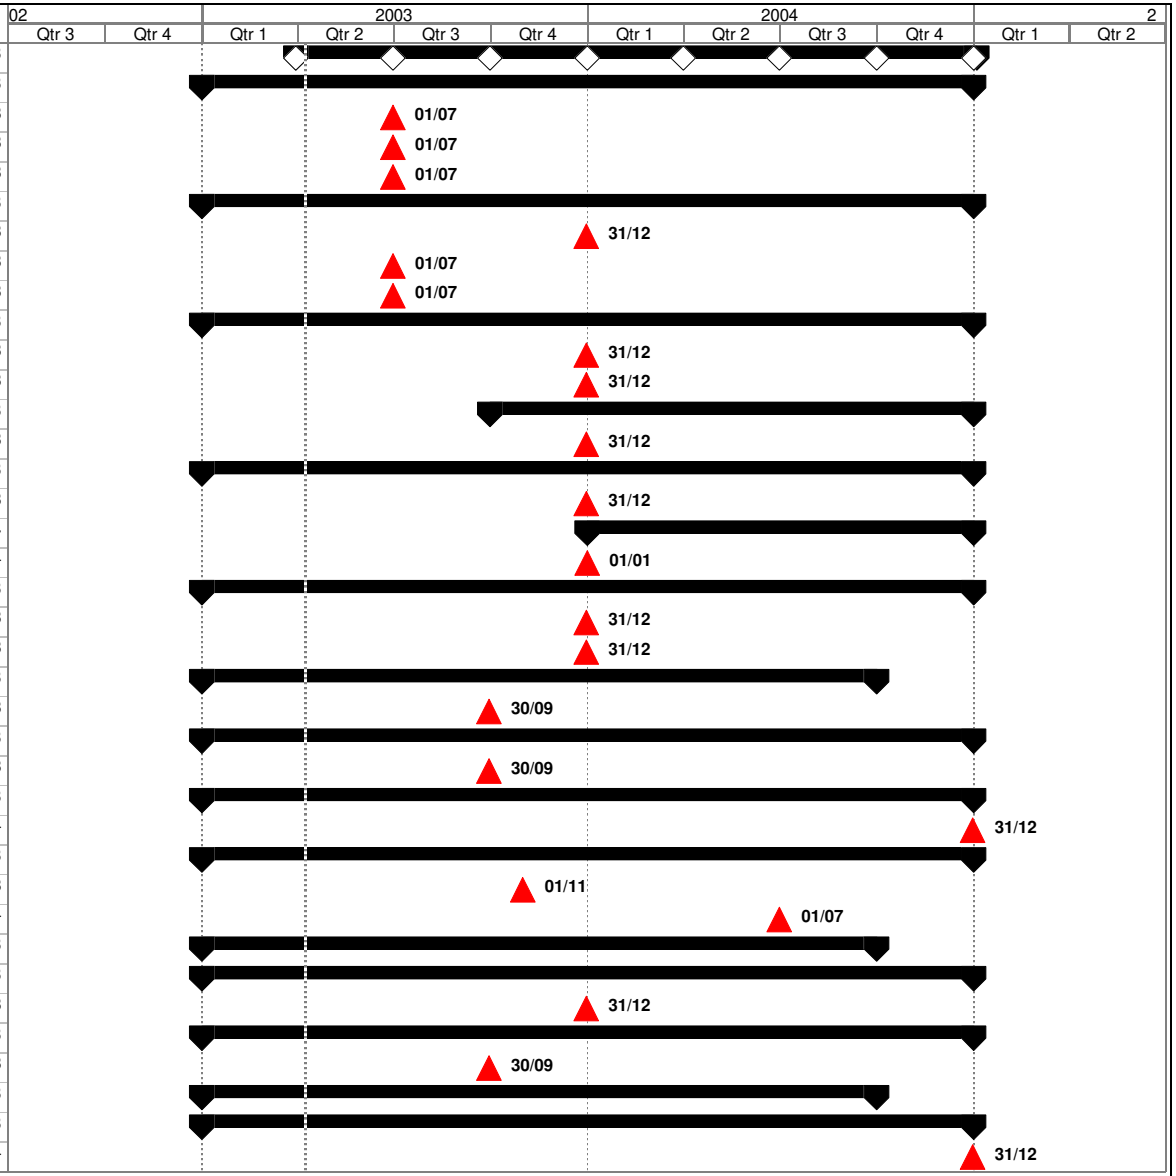

Project: vdfs
Date: Tue 08/04/03

Task
Progress
Milestone
Summary
Rolled Up Task
Rolled Up Milestone
Rolled Up Progress
Split
External Tasks
Project Summary
Group By Summary
